



# Appendix 1 Prestatyn coastal flood alleviation scheme location, design and consultation timeline


## 1a Prestatyn frontage

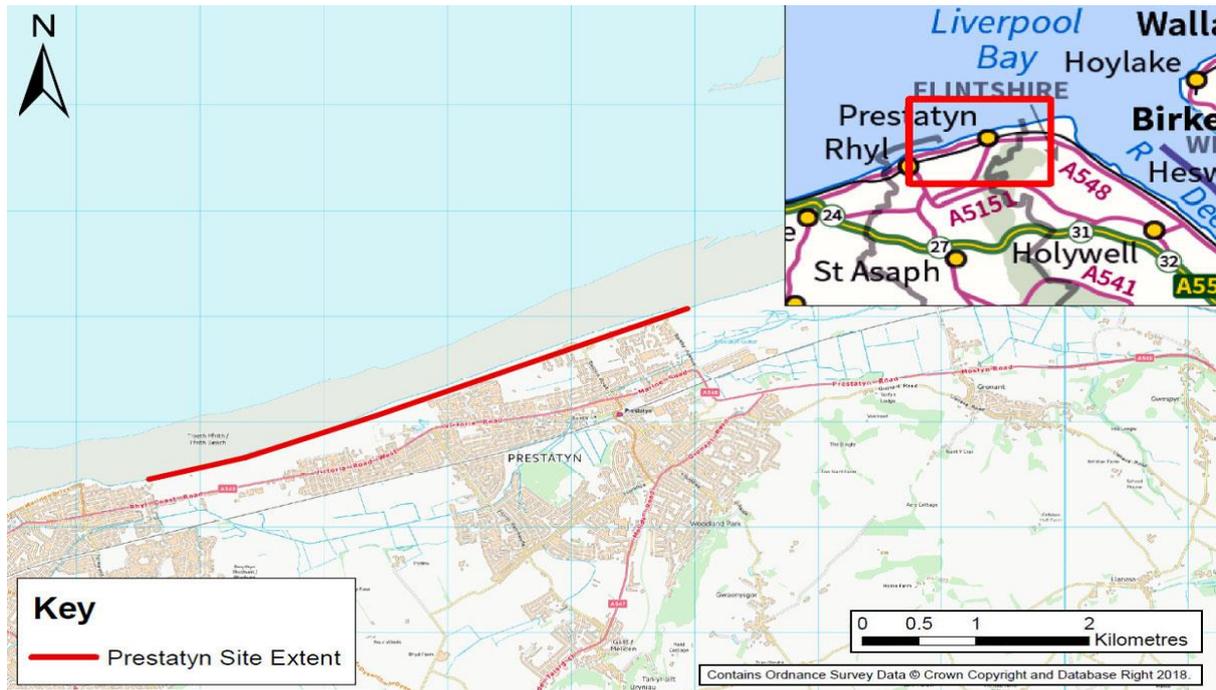

Although the entire frontage (shown by the red line in the location plan above) will eventually need improvements, the Central Prestatyn Coastal Defence Scheme focuses on the area of most immediate concern, adjacent to Rhyll Golf Club: see below

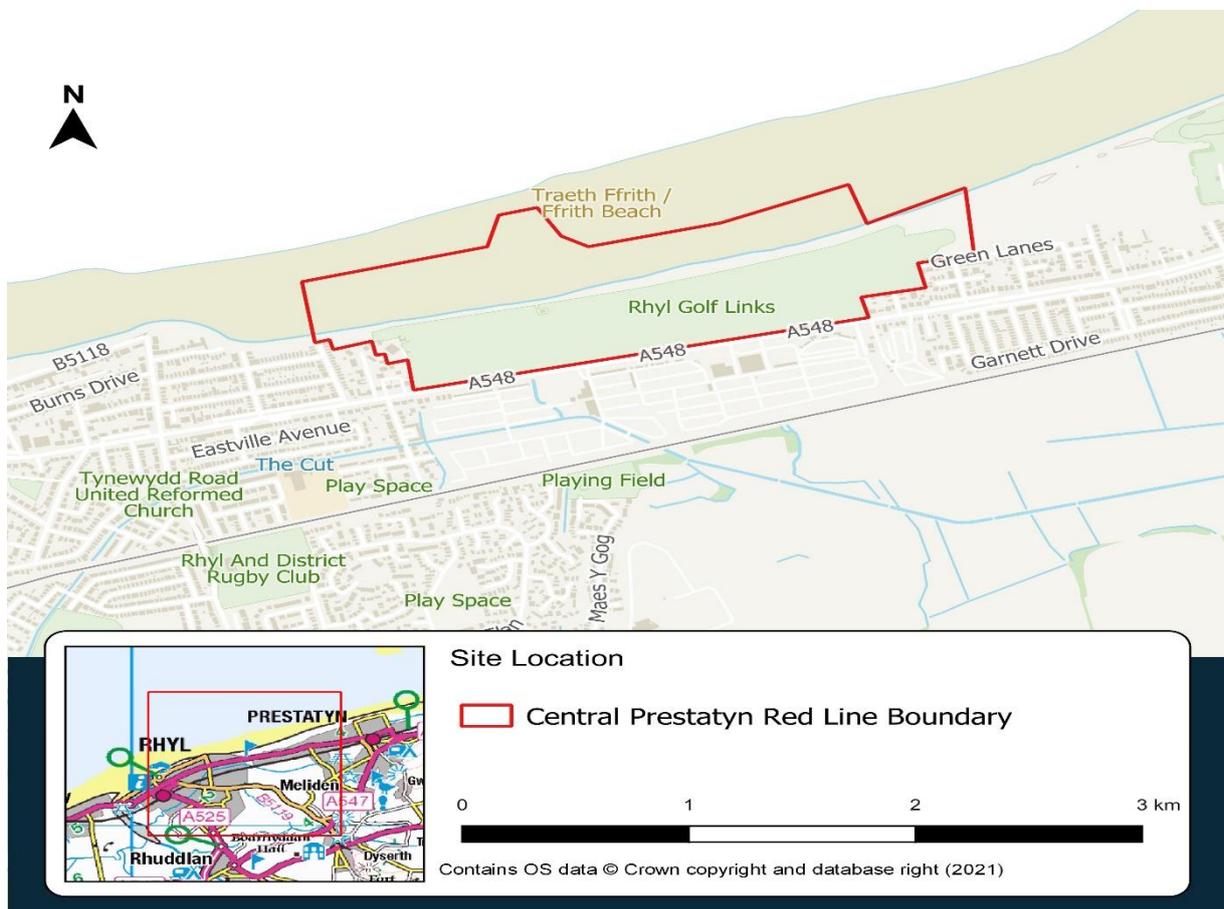

# 1a Cont'd Prestatyn flood risk map adjacent to Rhyl Golf Club

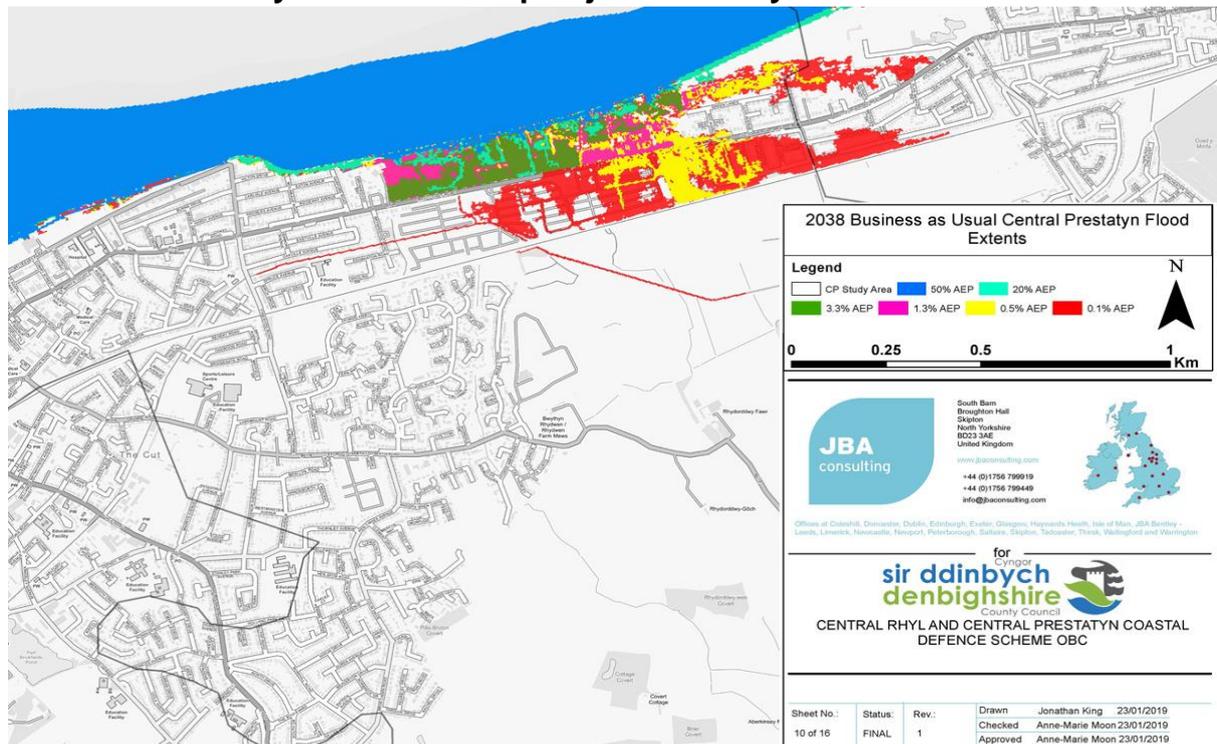

# 1b Prestatyn coastal flood alleviation design



## 1c Prestatyn stakeholder engagement timeline

The below details key engagement in 2021 up to the submission date for scrutiny, 25<sup>th</sup> Nov 2021.

Incidences of where an adaptive approach to design and consultation are highlighted in bold

<b>Date</b>	<b>Stakeholder</b>	<b>Reason</b>	<b>Response</b>
<b>10/12/21</b>	Scrutiny	Advice on consultation	Engage with local MAG's
<b>01/03/21</b>	Cabinet Briefing	Update on schemes and discussion about proceeding to planning	Proceed to planning application stage with no guarantee of funding of the schemes. Future cabinet briefing update required
<b>19/04/21</b>	Prestatyn MAG	Presentation on the scheme design and issues	More information required on the reasoning for the location of the scheme. A special MAG meeting to be scheduled for June
<b>27/05/21</b>	Rhyl Golf Club	Discuss the design option and construction methodology	RGC understood the need for the design but require more info on the methodology and how it will affect the club. Joint press release issued on how DCC and RGC are working together. Regular meetings put in place and Councillors Tony Thomas and Barry Mellor were updated about the meeting.
<b>30/06/21</b>	Special Prestatyn MAG	Special meeting to go through technical aspects of the design	Low attendance, those raising issues previously were not present. Design and information were sent to non-attendees but no responses received.
<b>31/08/21</b>	Rhyl Golf Club	Discuss the construction method of the scheme	RGC were made aware that the construction method would require closure of the club at certain times. RGC asked for work to start in Oct / Nov rather than in the Spring. This has been taken on board.
<b>20/09/21</b>	Rhyl MAG	Update on Prestatyn scheme	Rhyl members received the presentation and understood the nature of the project.
<b>28/10/21</b>	Rhyl Golf Club	Ongoing discussions	DCC continues to have productive discussions with RGC
<b>16/11/21</b>	Prestatyn MAG	Update on Prestatyn scheme	Meeting cancelled due to ICT issues. Will request to attend future meeting instead.

Future planned engagement includes: Cabinet Briefing 06/12/21, Strategic Investment Group (SIG) 14/12/21, Cabinet 18/01/22, Full Council 22/02/22, re-scheduled MAG (date tbc).
